

Project Plan

TaskFlow — Personal & Collaborative Project Management Platform

Timeline (Gantt Chart) • Milestones • Deliverables • Resource Allocation

DOCUMENT DETAILS

PROGRAM
DEPI

PROJECT
TaskFlow

VERSION
1.0

PREPARED
14 October 2026

TEAM SIZE
5 members

AI
Out of scope

Plan • Organize • Achieve

Scope allocation note: The public marketing pages (Landing Page, Features/How It Works, Pricing, and optional marketing Contact/FAQ pages) are handled separately by Mostafa and are excluded from the shared module/resource allocation below. The plan covers the authenticated TaskFlow application and its internal modules.

1 Project Overview

TaskFlow is a project and task management platform for individuals, freelancers, small teams, and companies. The planned scope includes personal/shared workspaces, projects, Kanban, task management, Gantt scheduling, time tracking, real-time collaboration, notifications, reporting, optional client access, Project Live Room, deliverable review, change requests, work handover, and rule-based project-health alerts.

The plan follows the DEPI dates supplied by the team. Detailed implementation windows are proposed working estimates and must be reviewed against the team's progress and instructor feedback.


2 DEPI Overall Timeline

Workstream	Start Date	End Date	Main Deliverables	Lead / Accountable Role
Project Planning & Management	2 Oct 2026	16 Oct 2026	Proposal, project plan, task assignment, risk plan, KPIs	Mostafa / Team Lead
Literature Review	9 Oct 2026	16 Oct 2026	Review of relevant tools, concepts, and competitor approaches	Mostafa coordinates; all members contribute
Requirements Gathering	9 Oct 2026	16 Oct 2026	Stakeholders, user stories/use cases, functional and non-functional requirements	Mostafa coordinates; module owners contribute
System Analysis & Design	9 Oct 2026	6 Nov 2026	Architecture, database design, workflow and system diagrams	Mostafa coordinates; all module owners contribute
Implementation (Source Code & Execution)	16 Oct 2026	30 Nov 2026	Working application and execution evidence	All members; each owns assigned module
Final Presentation, Testing & Reports	16 Oct 2026	4 Dec 2026	Test plan/results, final report, presentation and demo	All members; Mostafa coordinates

The workstreams overlap intentionally. Testing, documentation, and presentation preparation start during implementation and continue until final submission.

3 Gantt Chart

The chart uses the official DEPI workstream dates and proposed module implementation windows.

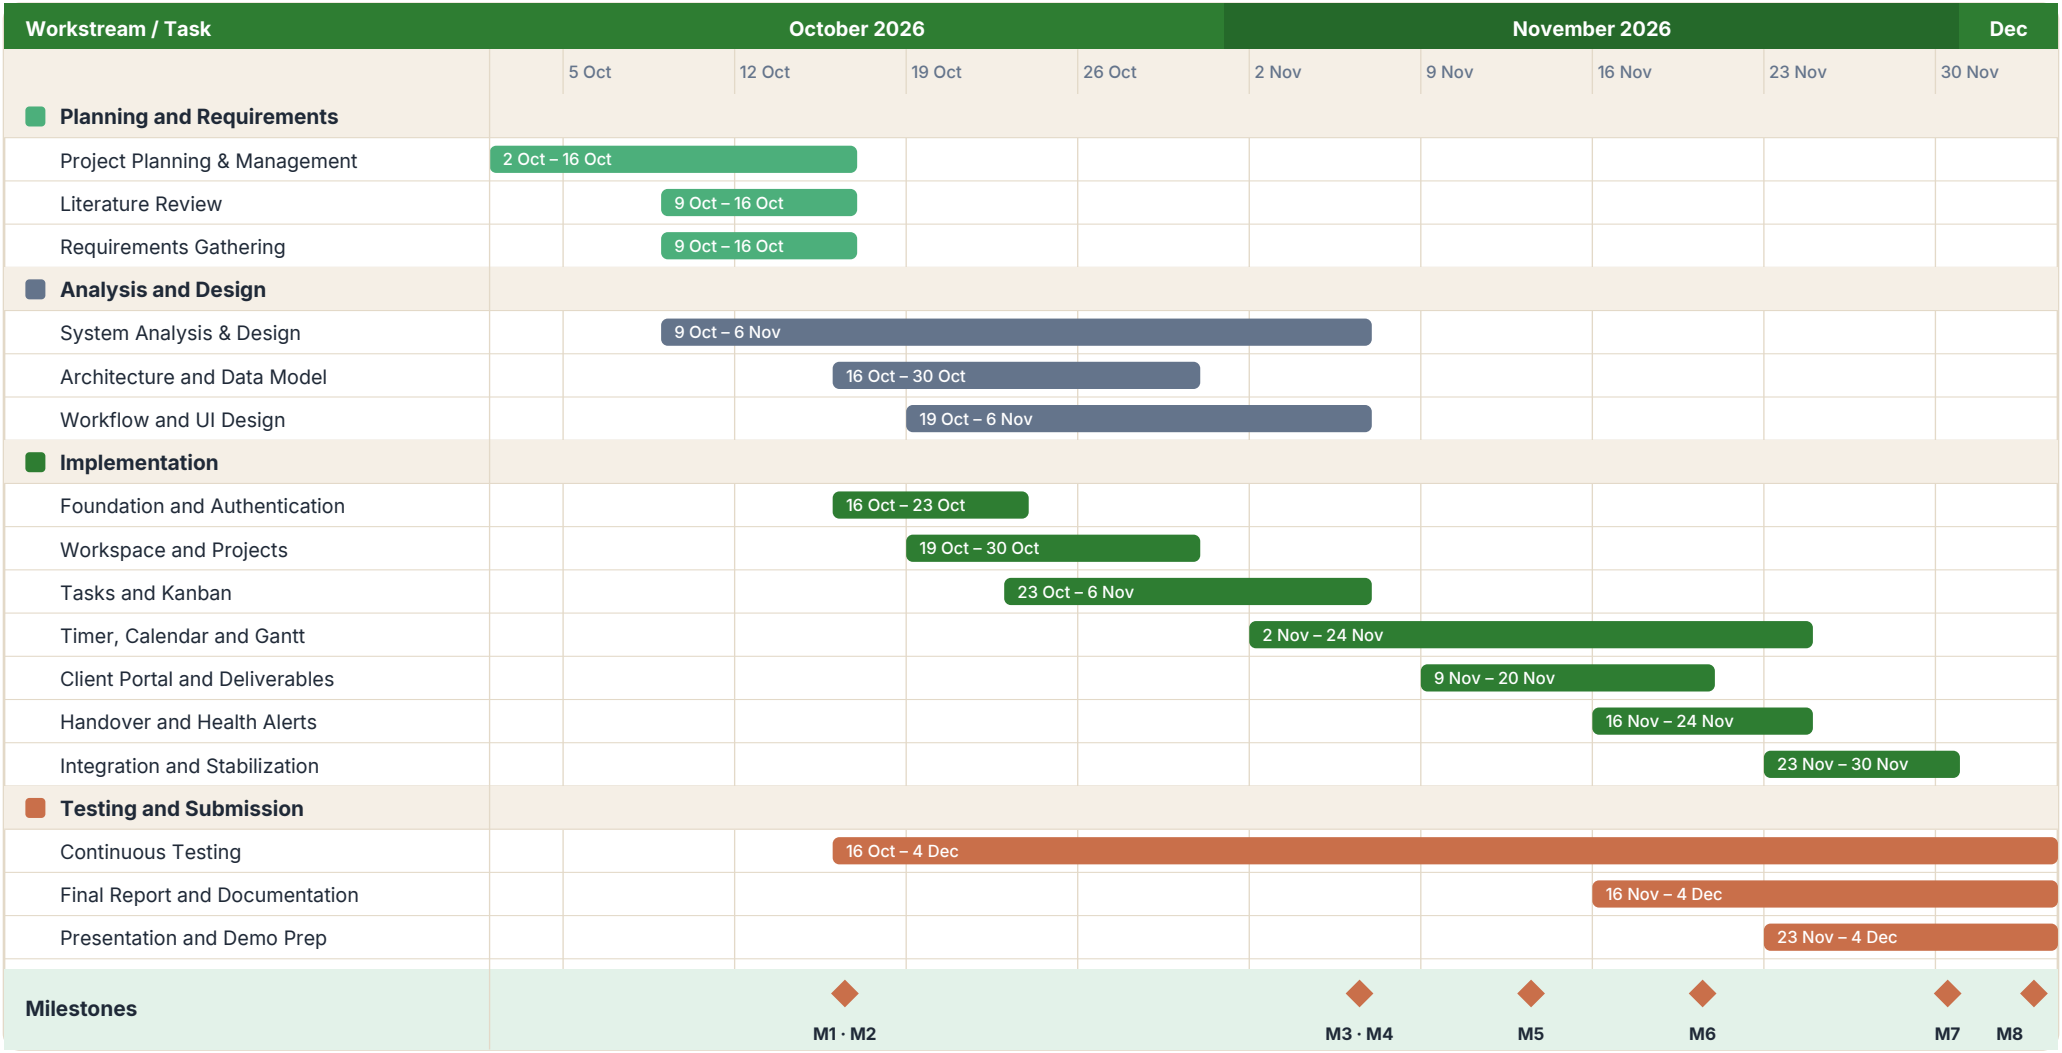

4 Work Packages and Responsibilities

ID	Work Package	Planned Window	Accountable Member	Main Activities	Completion Evidence
WP1	**Platform foundation and authentication**	16–23 Oct	**Mostafa Mohamed Mahmoud Mohamed**	Solution structure, Identity, login/register, account flows, shared conventions and integration setup	App runs locally; authentication and initial migrations work
WP2	**Workspaces, teams and projects**	19–30 Oct	**Ahmed Reda Ahmed Sedik**	Workspace/project CRUD, memberships, invitations, role/access UI, project setup and templates	Users create workspaces/projects and cannot access unauthorized projects
WP3	**Tasks, Kanban and task collaboration**	23 Oct–6 Nov	**Alaa Essam Hamed Abdelkader**	Tasks, columns, priorities, due dates, assignees, subtasks, checklists, comments, attachments, task history, handover notes	Task lifecycle is saved and tested; Kanban movement updates data correctly
WP4	**Time tracking, scheduling and project health**	2–24 Nov	**Ahd Ammar Eisa El-Baqary**	Timer lifecycle, time entries, timesheets, calendars, Gantt, dependencies and rule-based health alerts	Timer and time totals pass test cases; schedule and agreed alerts are demonstrable
WP5	**Client portal and delivery workflow**	9–20 Nov	**Eman Mohamed Masad El-Metwally**	Client records/access, Project Live Room, shared progress, deliverable versions/reviews, feedback and change requests	Client sees only authorized project data; review and change-request flows work
WP6	**Cross-module integration and stabilization**	23–30 Nov	**Mostafa coordinates; all module owners fix their areas**	Integrate modules, resolve defects, verify authorization, review migrations and prepare release candidate	Core scenarios work end-to-end; critical defects are resolved or explicitly documented
WP7	**Final testing, reports and presentation**	16 Oct–4 Dec	**All members; Mostafa coordinates**	Test cases, regression, final report, user/setup documentation, slides and demo rehearsal	Test evidence, GitHub documents, final demo and presentation are ready

Dependency note: WP4 depends on the Task entity and agreed interfaces from WP3; WP5 depends on Project/access contracts from WP2 and task/deliverable integration points from WP3. UI scaffolding can start earlier, but integration must use the shared contracts agreed by the owners.

5 Milestones

ID	Milestone	Target Date	Owner	Acceptance Criteria / Evidence
M1	**Planning package completed**	16 Oct 2026	Mostafa + all members	Proposal, plan, roles, risk assessment and KPI documents are uploaded to GitHub and reviewed
M2	**Requirements baseline completed**	16 Oct 2026	Mostafa coordinates; all contribute	Stakeholders, user stories/use cases, functional and non-functional requirements are reviewed
M3	**Architecture and design review**	6 Nov 2026	Mostafa coordinates; all module owners	Architecture, ERD/database design and main workflow diagrams are documented and reviewed
M4	**Core project and task workflow**	6 Nov 2026	Ahmed + Alaa	Authorized user can create a project, create tasks, and move tasks through Kanban with persistence
M5	**Time tracking and collaboration**	13 Nov 2026	Ahd + Alaa + Mostafa	Timer start/pause/resume/stop cases work; saved time is correct; comments/real-time updates follow access rules
M6	**Client delivery workflow**	20 Nov 2026	Eman	Client access is restricted; shared deliverable can be reviewed; decision and change request are recorded
M7	**Release candidate / implementation freeze**	30 Nov 2026	All; Mostafa coordinates	Agreed scope is integrated, deployment/setup instructions are available, and critical defects are resolved or documented
M8	**Final submission**	4 Dec 2026	All; Mostafa coordinates	Test results, final report, GitHub repository, presentation and demo are ready

6 Deliverables

6.1 Documentation Deliverables

- Project Proposal.
- Project Plan with Gantt chart, milestones, deliverables and resource allocation.
- Task Assignment & Roles.
- Risk Assessment & Mitigation Plan.
- KPIs.
- Literature Review.
- Stakeholder Analysis, User Stories and Use Cases.
- Functional and Non-functional Requirements.
- System architecture and database design diagrams.
- Test plan, test cases, test results, setup guide, and user guide.
- Final report and presentation materials.

6.2 Software Deliverables

- Authenticated TaskFlow web application with personal and optional shared workspaces.
- Project and task management, including Kanban and the agreed Gantt functionality.
- Time tracking with persisted sessions and summary reports.
- Comments, attachments, notifications, activity history, and authorized real-time updates.
- Optional client portal and Project Live Room.
- Deliverable versions, review decisions, feedback, and change-request workflow.
- Handover notes and rule-based project-health alerts, subject to the agreed final scope.
- Source code, configuration template, database migrations, and reproducible setup instructions in GitHub.
- Working demonstration of the critical end-to-end scenarios.

7 Resource Allocation

The percentages below are **estimated effort shares for the authenticated application/module work**, not confirmed hours or official requirements. Public marketing pages implemented separately by Mostafa are excluded from these percentages and from the shared module assignments.

Team Member	Role / Module Ownership	Estimated Share of Core-App Effort	Main Resources / Tools	Key Dependencies
Mostafa Mohamed Mahmoud Mohamed	Team Lead; authentication, account flows, shared platform foundation, notification/SignalR conventions, integration coordination	**18%**	ASP.NET Core Identity, shared services, GitHub PRs, architecture and release checklist	Coordinates interfaces and integration with all members
Ahmed Reda Ahmed Sedik	Workspace, teams, memberships, invitations, permissions UI, projects, project settings and templates	**21%**	ASP.NET Core MVC, EF Core, SQL Server, project/workspace entities	Identity contracts from Mostafa; task/board references from Alaa; client access coordination with Eman
Alaa Essam Hamed Abdelkader	Task lifecycle, Kanban, subtasks/checklists, comments, attachments, task activity and handover notes	**22%**	MVC/JavaScript, Dragula.js, EF Core, SignalR shared interface	Project and membership entities from Ahmed; task contract for Ahd and Eman
Ahd Ammar Eisa El-Baqary	Timer, time entries, timesheets, calendar, Gantt, dependencies, time reports and project-health alerts	**19%**	EF Core, Frappe Gantt, Chart.js, timer/test scenarios	Task and Project contracts from Alaa/Ahmed; deliverable state events from Eman where used
Eman Mohamed Masad El-Metwally	Client portal, Project Live Room, client access, deliverables, reviews, change requests	**20%**	ASP.NET Core MVC, EF Core, file storage interface, review/approval test scenarios	Project membership/access from Ahmed; task/attachment contracts from Alaa; time-summary interface from Ahd
Total		**100%**		

These estimates should be adjusted after the team compares members' experience and actual availability. The percentages indicate planned effort distribution, not the number of pages each person owns. Mostafa's separate public-page work is an additional responsibility outside this allocation.

Shared Resources

- **Repository:** GitHub, feature branches, pull requests, code review, and Issues for blockers/defects.
- **Development stack:** ASP.NET Core MVC, C#, Entity Framework Core, ASP.NET Core Identity, SQL Server/Azure SQL, Bootstrap, JavaScript, SignalR, and selected UI libraries.
- **Design and documentation:** Shared page map, ERD, acceptance criteria, README, architecture notes, and consistent UI components.
- **Testing:** Each member tests their module; all five members participate in end-to-end regression tests.
- **Deployment:** Azure if approved and available; otherwise an agreed demo environment with configuration documented.

8 Progress Tracking and Communication

- Each task in GitHub Issues should have an owner, priority, acceptance criteria, and target milestone.
- Each member owns the frontend, backend logic, data changes, validation, and test evidence for their assigned module.
- Use feature branches and pull requests; avoid multiple people editing the same migration or shared entity file without coordination.
- The member who owns a module is responsible for fixing defects in that module.
- Review progress against milestone acceptance criteria rather than using percentage-complete estimates alone.
- Update documentation whenever the implemented behavior or approved scope changes.

9 Scope Control and Contingency

If the schedule becomes at risk, protect this minimum demonstrable workflow first:

1. Authentication and safe workspace/project access.
2. Project creation and task lifecycle through Kanban.
3. Correct timer persistence and time summary.
4. Client can access only a shared project and review an available deliverable.
5. Key test evidence, setup documentation, and final demo.

> Advanced dependency/critical-path calculations, extensive analytics, subscription billing, complex custom automation, and optional polish can be deferred if needed. A deferred feature must be recorded in GitHub with a reason rather than represented as completed.

10 Approval and Review

Reviewer	Name	Status / Date
Team Lead	Mostafa Mohamed Mahmoud Mohamed	Pending team review
Team Representative	To be assigned	Pending
DEPI Instructor / Reviewer	To be assigned	Pending
